
NIRMAN AI · KAAMTRACK BY FLODATA ANALYTICS

FLODATA ANALYTICS

Nirman AI: From site conversation to tomorrow's work program.

A voice-led daily coordination layer within KaamTrack.

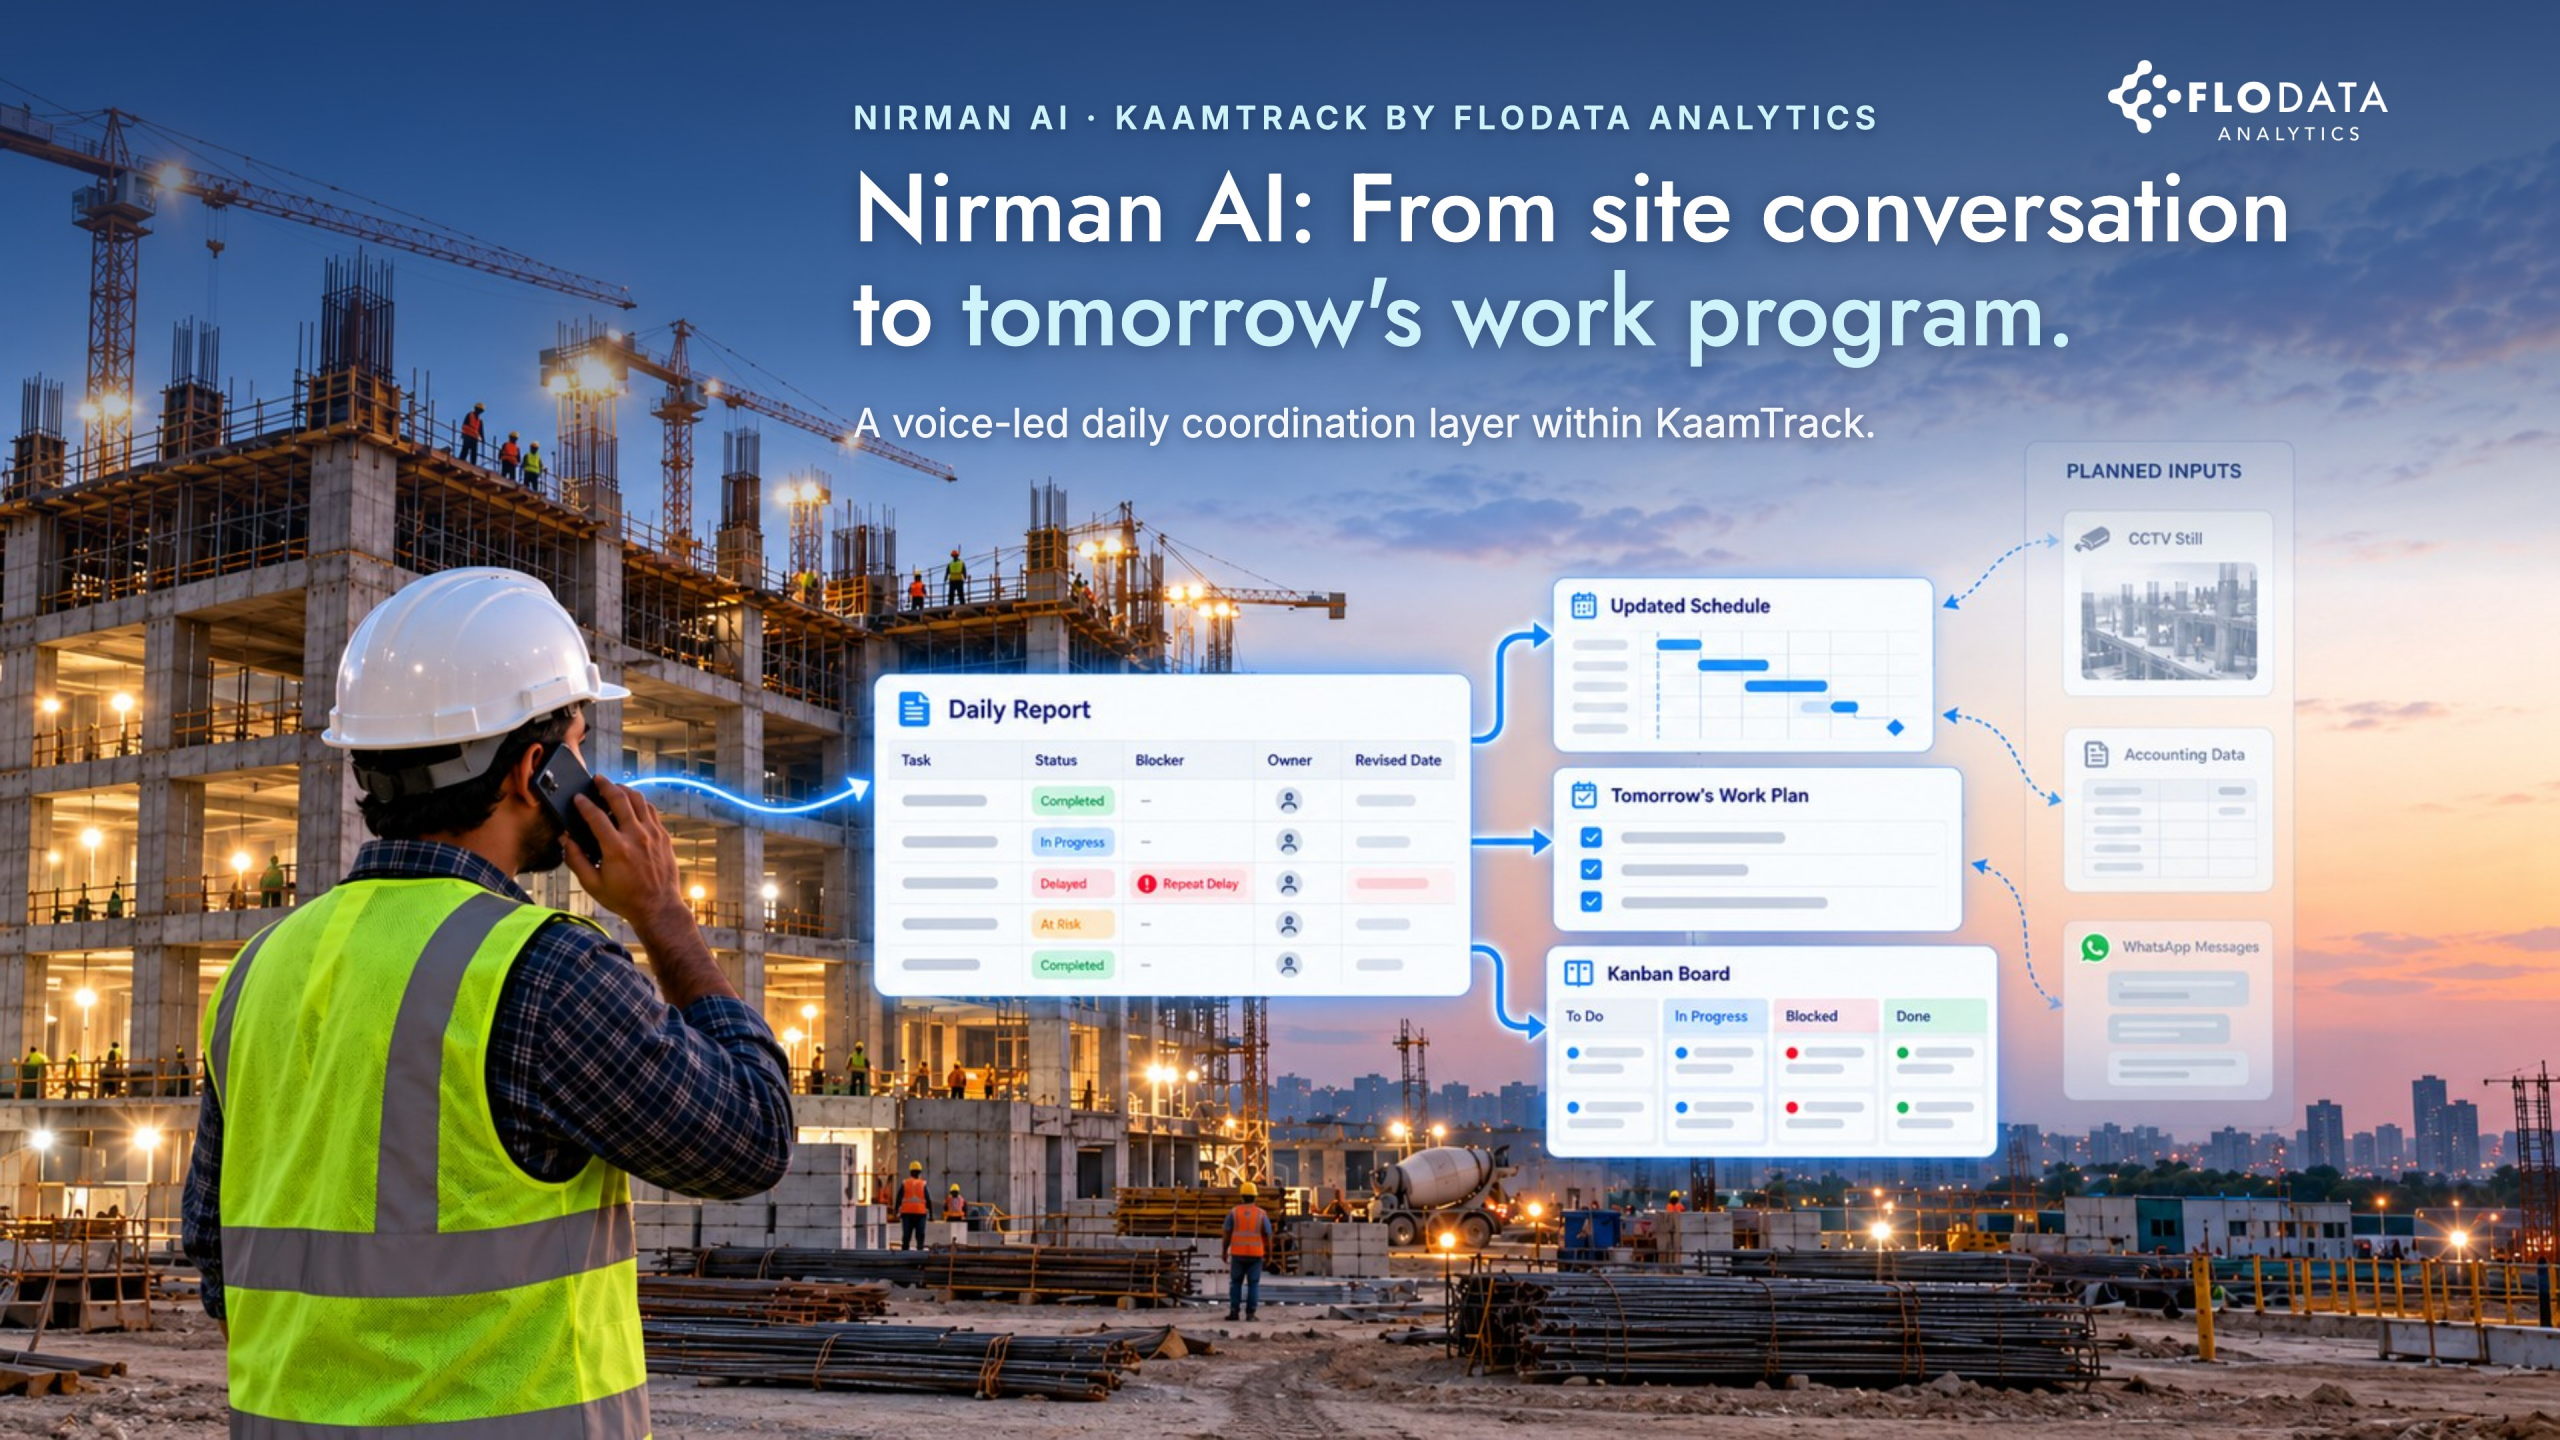

THE DAILY COORDINATION GAP

At day's end, the plan and the site rarely match.

PLANNED TODAY

SW3 and column shuttering

SW4 reinforcement

Columns 27 and 28 reinforcement

Column 14 casting

WHAT THE SITE REPORTS

"Shuttering is up. Supports are still left."

"Supports will take all of tomorrow."

"SW4 and columns 27, 28 are done."

NEEDED FOR TOMORROW

Revised dates

Crews and material lined up

Delays escalated

NIRMAN AI RESOLVES, EVERY EVENING

What finished?	What slipped?	Material, labour or other?
Who owns it?	When will it finish?	What needs management?

HOW THE CURRENT SOLUTION WORKS

One call in. Tomorrow's program out.

CURRENT WORKING SOLUTION

01
Voice update
Supervisor or PM talks through the day

02
Map to plan
Each remark matched to today's program

03
Assess tasks
Done, partial, blocker, owner, new date

04
Reschedule
Revised dates go to the scheduler

05
Plan tomorrow
Work program and Kanban update

06
Flag for manager
Delays, unassigned work and repeat slips

SHOWN NEXT ON A REAL CALL **4 completed** **1 open, due tomorrow** **0 flags**

A LIVE SITE CALL · 13 OCTOBER 2026

One call. A site report by evening.

CURRENT WORKING SOLUTION

CALL TRANSCRIPT, EXCERPTS

Nirman AI Carpenter ka shuttering, SW3 aur columns?

Site लगा दिया है। अभी support fix करना बाकी है।

Nirman AI Support fix karne mein kitna time?


Site कल पूरा दिन लग जाएगा।

Nirman AI Barbender, SW4 binding aur columns?

Site Resilium 4 complete। Columns 27 और 28 भी हो गए।

Nirman AI Koi issue, koi extra kaam?

Site नहीं, कुछ नहीं था।

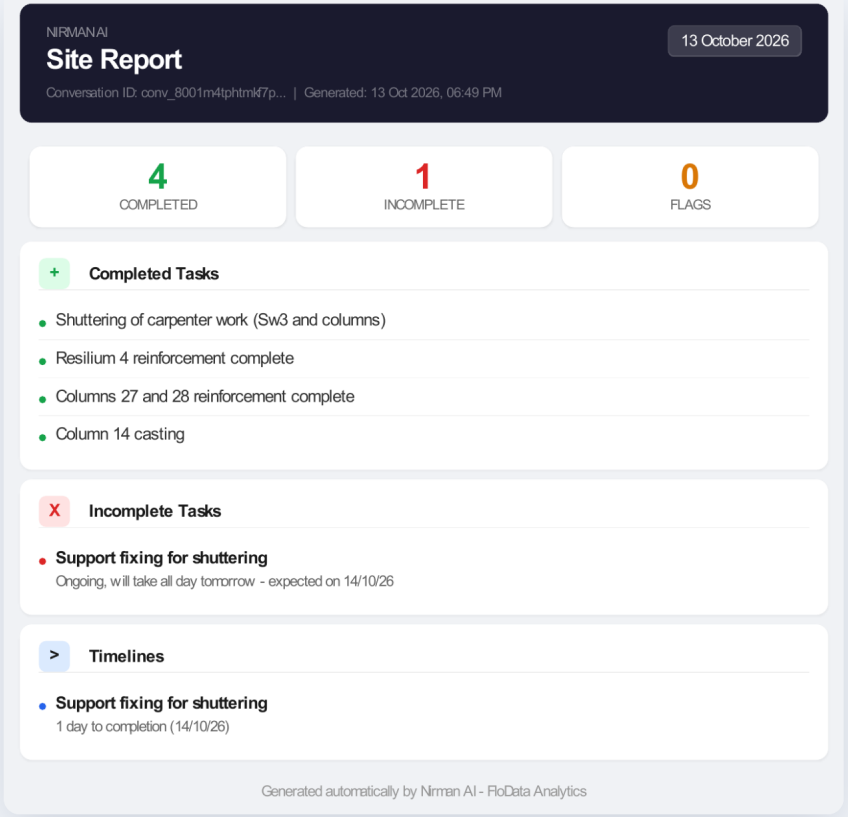

NIRMAN AI

Site Report

13 October 2026

Conversation ID: conv_8001m4tphtmkf7p... | Generated: 13 Oct 2026, 06:49 PM

4	1	0
COMPLETED	INCOMPLETE	FLAGS

+ Completed Tasks

- Shuttering of carpenter work (Sw3 and columns)
- Resilium 4 reinforcement complete
- Columns 27 and 28 reinforcement complete
- Column 14 casting

X Incomplete Tasks

- **Support fixing for shuttering**
  Ongoing, will take all day tomorrow - expected on 14/10/26

> Timelines

- **Support fixing for shuttering**
  1 day to completion (14/10/26)


Generated automatically by Nirman AI - FloData Analytics

The actual report, generated at 6:49 PM the same evening

THREE DAYS ON ONE SITE · 12 TO 14 OCTOBER 2026

Dates given on the call. Checked the next day.

TASK	12 OCT	13 OCT	14 OCT
SW4 reinforcement binding	40 to 50% done. Expected 13/10	**Completed.** Date held	
SW3 shuttering supports	Shuttering done. Supports expected 14/10	**SW3 complete.** Casting tonight	
Column 13 binding	**Not assigned.** Flagged		

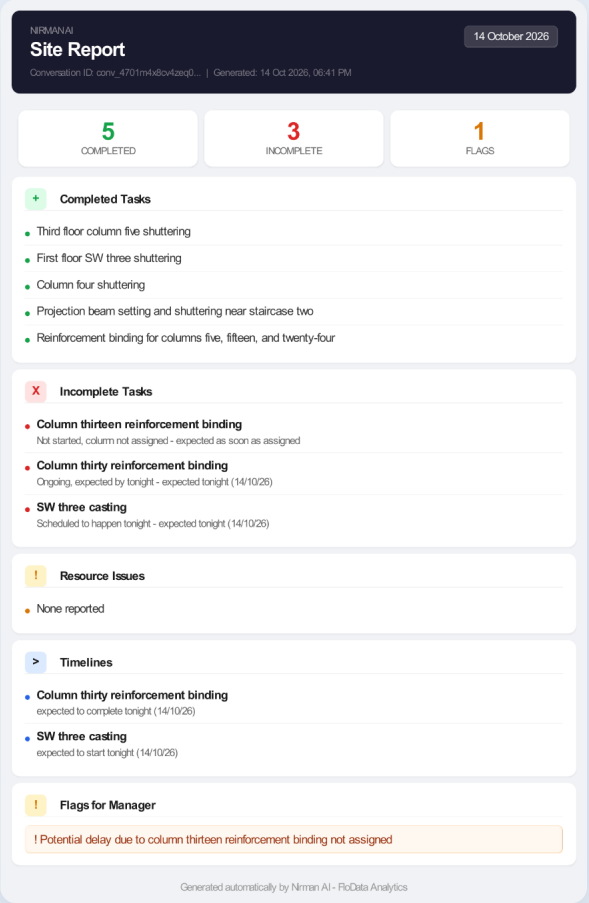

The actual report, 14 October 2026

PROMOTER DASHBOARD · SAME SITE, 1 TO 14 OCTOBER 2026

One daily view. Clearer action for the next day.

TODAY · 14 OCTOBER

5	3	1
Completed	Incomplete	Flag

FLAG FOR MANAGER

Column 13 reinforcement not assigned. Potential delay.

TONIGHT

SW3 casting · column 30 binding

NEEDED YOUR ATTENTION, WITHOUT A CALL

01 Oct	Third floor shuttering is a priority. Finish in 2 days
07 Oct	Manpower short for STP wall shuttering. Contractor responsible
08 Oct	Ramp material shifting to finish by 09/10
12 Oct	Lightweight blocks finished, new supply awaited. Thekedar responsible
14 Oct	Column 13 reinforcement not assigned

PILOT AND ROADMAP

Know what's happening on your site. Without making the calls.

PILOT · LIVE TODAY

2 weeks

Try Nirman AI on one active project. See what gets completed, what slips, who is responsible and what needs your attention tomorrow.

One project · Daily voice updates · Measurable pilot

MEASURED AGAINST WEEK ONE

- Follow-up calls to site
- Time on daily reporting
- Slips caught the same day
- Schedule dates that held

ROADMAP · PLANNED

Evidence behind every report

CCTV snapshots

Corroborate what the site reports

Accounting data

Add the financial picture

WhatsApp messages

Keep the context behind decisions
